



**THE RISING FOUNDATION**  
EMPOWER PEOPLE TO IMPROVE THEIR LIVELIHOOD



## **Project Completion Report (Phase-2)**

**Service Consultancy for Provision of Fodder for Livestock of  
Monsoon Rain Flood Calamity Hit Areas of Sindh Province –  
For the Department of Livestock & Fisheries,  
Government of Sindh.**



**THE RISING FOUNDATION**  
EMPOWER PEOPLE TO IMPROVE THEIR LIVELIHOOD



---

## Table of Contents

|                                                                    |    |
|--------------------------------------------------------------------|----|
| SERVICES CONSULTANCY FOR FODDER DISTRIBUTION .....                 | 2  |
| <b>Background</b> .....                                            | 2  |
| <b>The Project</b> .....                                           | 3  |
| <b>Operational Objectives of the Project</b> .....                 | 3  |
| <b>Project Implementation Timeline</b> .....                       | 3  |
| <b>Geographical outreach of the Project</b> .....                  | 5  |
| <b>Implementation Strategy</b> .....                               | 5  |
| <b>Project Completion Progress – Phase 2</b> .....                 | 8  |
| <b>Distribution Proforma &amp; Fodder Distribution Token</b> ..... | 13 |
| <b>Project Completion (Phase 2)</b> .....                          | 15 |
| <b>Fodder Distribution Status across 23 Districts</b> .....        | 17 |
| <b>Beneficiaries Outreach vis-a-vie Livestock Catered</b> .....    | 20 |
| <b>Project's Photo Gallery</b> .....                               | 21 |



## SERVICES CONSULTANCY FOR FODDER DISTRIBUTION

| Reporting Period                         | 1 <sup>st</sup> December 2022 to 28 <sup>th</sup> February 2023                                                                                                                                                                                                                                 |
|------------------------------------------|-------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------|
| Names of Operational DPIUs District-wise | Badin, Dadu, Ghotki, Hyderabad, Jacobabad, Jamshoro, Khairpur Mir's, Kashmore-Kandhkot, Larkana, Malir (Karachi), Matiari, Mirpurkhas, Naushehro Feroze, Qamber/Shahdadkot, Sanghar, Shaheed Benazirabad, Shikarpur, Sujawal, Sukkur, Tando Allahyar, Tando Muhammad Khan, Thatta, and Umerkot. |
| Type of Report                           | Project Completion Report – Phase 2                                                                                                                                                                                                                                                             |

### Background

The current wave of heavy monsoon rainfalls and flash floods throughout Pakistan especially Sindh province has badly affected, houses, standing crops of Kharif, human lives as well as Livestock & Poultry. Government of Sindh vide Notification No. R/F-272/2022 Hyderabad dated 21.08.2022 has declared **calamity affected areas of 23 Districts of Sindh Province** i.e., Hyderabad, Badin, Thatta, Sujawal, Jamshoro, Tando Muhammad Khan, Tando Allahyar, Matiari, Dadu, Mirpurkhas, Umerkot, Shaheed Benazirabad, Naushehro Feroze, Sukkur, Khairpur, Ghotki, Larkana, Kashmore, Shikarpur, Kamber-Shahdadkot, Jacobabad, Sanghar and two Dehs of Malir Karachi (hereinafter referred as calamity affected areas). Millions of heads of small & large Livestock ruminants have been affected/displaced. The stock of dry fodder like wheat chaff and hay either is spoiled due to heavy rainfall or is inaccessible, leaving livestock of Sindh without fodder on the banks of canals, river and roadsides. The farmers and rural community have suffered badly in terms of crops, lives, property loss and only hope for their livelihood and revival is their livestock.

In wake of the calamity, Sindh government has sanctioned an immediate response by releasing an emergency grant to create access of farmers for fodder for their animals through the department of Livestock and Fisheries, Government of Sindh.



## The Project

Hence, the department of Livestock and Fisheries advertised for quotes to provide consultancy of services and The Rising Foundation (TRF) was selected from among the contestants. The contract agreement was signed on 7<sup>th</sup> October 2022 between the representatives of The Rising Foundation (TRF) and the Department of Livestock and Fisheries, Government of Sindh for the Project **“Provision of Fodder for Livestock of Monsoon Rain Flood Calamity Hit Areas of Sindh Province”**. The Rising Foundation (TRF) will deliver the interventions under this project in the 23 districts of Sindh province.

## Operational Objectives of the Project

Following are the operational objectives of the Program assigned to The Rising Foundation (TRF):

- Fodder Beneficiary Mapping Survey to be conducted in 23 districts of Sindh.
- Distribution of Fodder to the beneficiaries as per finalized beneficiary lists across 23 districts of Sindh.

## Project Implementation Timeline

| Project Time Frame                             |       |       |       |       |       |       |        |       |        |        |        |        |        |        |
|------------------------------------------------|-------|-------|-------|-------|-------|-------|--------|-------|--------|--------|--------|--------|--------|--------|
| Total Project Tenure:<br>3 Months              |       |       |       |       |       |       |        |       |        |        |        |        |        |        |
| Week 1                                         |       |       |       |       |       |       | Week 2 |       |        |        |        |        |        |        |
| Day 1                                          | Day 2 | Day 3 | Day 4 | Day 5 | Day 6 | Day 7 | Day 8  | Day 9 | Day 10 | Day 11 | Day 12 | Day 13 | Day 14 | Day 15 |
| 1 DEC                                          | 2 DEC | 3 DEC | 4 DEC | 5 DEC | 6 DEC | 7 DEC | 8 DEC  | 9 DEC | 10 DEC | 11 DEC | 12 DEC | 13 DEC | 14 DEC | 15 DEC |
| Activities are planned in all days of the week |       |       |       |       |       |       |        |       |        |        |        |        |        |        |

| Project Tenure: 1st Month |        |        |        |        |        |        |        |        |        |        |        |        |        |        |        |
|---------------------------|--------|--------|--------|--------|--------|--------|--------|--------|--------|--------|--------|--------|--------|--------|--------|
| Week 3                    |        |        |        |        |        |        | Week 4 |        |        |        |        |        |        |        |        |
| Day 16                    | Day 17 | Day 18 | Day 19 | Day 20 | Day 21 | Day 22 | Day 23 | Day 24 | Day 25 | Day 26 | Day 27 | Day 28 | Day 29 | Day 30 | Day 31 |
| 16 DEC                    | 17 DEC | 18 DEC | 19 DEC | 20 DEC | 21 DEC | 22 DEC | 23 DEC | 24 DEC | 25 DEC | 26 DEC | 27 DEC | 28 DEC | 29 DEC | 30 DEC | 31 DEC |

**Project Completion Report (Phase-2):** Service Consultancy for Provision of Fodder for Livestock of Monsoon Rain Flood Calamity Hit Areas of Sindh Province – Project (Livestock Department Sindh).



| Activities are planned in all days of the week |        |        |        |        |        |        |        |        |        |        |        |        |        |        |
|------------------------------------------------|--------|--------|--------|--------|--------|--------|--------|--------|--------|--------|--------|--------|--------|--------|
| Project Time Frame                             |        |        |        |        |        |        |        |        |        |        |        |        |        |        |
| Total Project Tenure:<br>3 Months              |        |        |        |        |        |        |        |        |        |        |        |        |        |        |
| Week 5                                         |        |        |        |        |        |        | Week 6 |        |        |        |        |        |        |        |
| Day 32                                         | Day 33 | Day 34 | Day 35 | Day 36 | Day 37 | Day 38 | Day 39 | Day 40 | Day 41 | Day 42 | Day 43 | Day 44 | Day 45 | Day 46 |
| 1 JAN                                          | 2 JAN  | 3 JAN  | 4 JAN  | 5 JAN  | 6 JAN  | 7 JAN  | 8 JAN  | 9 JAN  | 10 JAN | 11 JAN | 12 JAN | 13 JAN | 14 JAN | 15 JAN |
| Activities are planned in all days of the week |        |        |        |        |        |        |        |        |        |        |        |        |        |        |

| Project Tenure: 2nd Month                      |        |        |        |        |        |        |        |        |        |        |        |        |        |        |        |
|------------------------------------------------|--------|--------|--------|--------|--------|--------|--------|--------|--------|--------|--------|--------|--------|--------|--------|
| Week 7                                         |        |        |        |        |        |        | Week 8 |        |        |        |        |        |        |        |        |
| Day 47                                         | Day 48 | Day 49 | Day 50 | Day 51 | Day 52 | Day 53 | Day 54 | Day 55 | Day 56 | Day 57 | Day 58 | Day 59 | Day 60 | Day 61 | Day 62 |
| 16 JAN                                         | 17 JAN | 18 JAN | 19 JAN | 20 JAN | 21 JAN | 22 JAN | 23 JAN | 24 JAN | 25 JAN | 26 JAN | 27 JAN | 28 JAN | 29 JAN | 30 JAN | 31 JAN |
| Activities are planned in all days of the week |        |        |        |        |        |        |        |        |        |        |        |        |        |        |        |

| Project Time Frame                             |        |        |        |        |        |        |         |        |        |        |        |        |        |        |
|------------------------------------------------|--------|--------|--------|--------|--------|--------|---------|--------|--------|--------|--------|--------|--------|--------|
| Total Project Tenure:<br>3 Months              |        |        |        |        |        |        |         |        |        |        |        |        |        |        |
| Week 9                                         |        |        |        |        |        |        | Week 10 |        |        |        |        |        |        |        |
| Day 63                                         | Day 64 | Day 65 | Day 66 | Day 67 | Day 68 | Day 69 | Day 70  | Day 71 | Day 72 | Day 73 | Day 74 | Day 75 | Day 76 | Day 77 |
| 1 FEB                                          | 2 FEB  | 3 FEB  | 4 FEB  | 5 FEB  | 6 FEB  | 7 FEB  | 8 FEB   | 9 FEB  | 10 FEB | 11 FEB | 12 FEB | 13 FEB | 14 FEB | 15 FEB |
| Activities are planned in all days of the week |        |        |        |        |        |        |         |        |        |        |        |        |        |        |

| Project Tenure: 3rd Month                      |        |        |        |        |        |        |         |        |        |        |        |        |   |   |   |
|------------------------------------------------|--------|--------|--------|--------|--------|--------|---------|--------|--------|--------|--------|--------|---|---|---|
| Week 11                                        |        |        |        |        |        |        | Week 12 |        |        |        |        |        |   |   |   |
| Day 78                                         | Day 79 | Day 80 | Day 81 | Day 82 | Day 83 | Day 84 | Day 85  | Day 86 | Day 87 | Day 88 | Day 89 | Day 90 | - | - | - |
| 16 FEB                                         | 17 FEB | 18 FEB | 19 FEB | 20 FEB | 21 FEB | 22 FEB | 23 FEB  | 24 FEB | 25 FEB | 26 FEB | 27 FEB | 28 FEB | - | - | - |
| Activities are planned in all days of the week |        |        |        |        |        |        |         |        |        |        |        |        |   |   |   |



## Geographical outreach of the Project

| Sr. # | Name of District             |
|-------|------------------------------|
| 1     | Badin                        |
| 2     | Dadu                         |
| 3     | Ghotki                       |
| 4     | Hyderabad                    |
| 5     | Jacobabad                    |
| 6     | Jamshoro                     |
| 7     | Kamber Shahdadkot            |
| 8     | Kashmore                     |
| 9     | Khairpur                     |
| 10    | Larkana                      |
| 11    | Malir (Karachi, only 2 Dehs) |
| 12    | Matari                       |
| 13    | Mirpurkhas                   |
| 14    | Naushehro Feroze             |
| 15    | Sanghar                      |
| 16    | Shaheed Benazirabad          |
| 17    | Shikarpur                    |
| 18    | Sujawal                      |
| 19    | Sukkur                       |
| 20    | Tando Allahyar               |
| 21    | Tando Muhammad Khan          |
| 22    | Thatta                       |
| 23    | Umerkot                      |

## Implementation Strategy

Following strategies for the delivery of the project objectives has been finalized for amicable completion of the project:

**Beneficiary Survey Strategy:** Competent data collection staff shall be hired on immediate basis from the rich pool of staff already available with us and with whom the management has already done prolific field interventions in and across 23 districts of Sindh province.

We will prefer to hire staff with veterinarian data collection experience with at least an undergraduate degree and otherwise social sector experience staff with undergraduate degree and relevant experience shall be hired across 23 districts of Sindh province. Final list of tentative staff will be shared with the competent authority accordingly.

**Fodder Logistic Support Strategy:** The logistics officer shall be responsible to create a logistics plan as per the distribution schedule provided by the Deputy Director L&F of a respective district. The logistics officer shall move the fodder transports accordingly as per the quantities of silage, wheat grass and Rhodes grass required. The logistics officer shall be responsible for the weighbridge receipts of the load before the unloading as well as afterwards. Logistics officer shall manage and will keep record of all the received fodder and the quantities delivered at the distribution point. The logistics officer will be responsible to deliver the required quantities as per the suggested weight of fodder by the respective Deputy Director L&F of the concerned district.

**Fodder Distribution Strategy:** The project shall commence its final part with simultaneous distribution of fodder in 23 districts of Sindh with and under the oversight and support of the field officers of the Livestock and Fisheries Department, Government of Sindh. Following are the general guidelines under which fodder distribution shall take place:

- A fodder distribution committee shall be constituted in which following members shall be added:
  1. Assistant Commissioner of the respective Taluka's
  2. Deputy Director, L&F of respective district
  3. Two notable persons of a district.
- The Deputy Commissioner of a respective district shall be notified of the respective Fodder Distribution Committee.
- Once the committee is formed and notified by the DC of the concerned district, a final list of the beneficiaries shall be sent to the Fodder Distribution Committee for review and approval. This list will also accompany the quantities of fodder to be distributed (Rhode Grass, Wheat Grass and Silage) with nos. of small and large animals.



- Once this list of beneficiaries is approved and received from the committee of a respective district, beneficiary tokens (tokens will be pre-numbered with two copies per token – copy of the token is attached for the review) shall immediately be created.
- Fodder Beneficiary Tokens shall be distributed among the fodder beneficiaries of a Taluka. The Fodder Beneficiary Tokens will confirm the date of distribution as well as the distribution location.
- Fodder distribution shall be called through a centrally located designated distribution point.
- The distribution point shall be managed in an organized manner by TRF with support and participation of the concerned Deputy Director Livestock of concerned district and their auxiliary staff. The distribution location shall hoist prominently a distribution banner of fodder distribution under the auspices of the Department of Livestock and Fisheries, Government of Sindh.
- The distribution of fodder will be carried out, while keeping the proceedings of distribution in an amicable manner consonant with keeping the pride of the beneficiaries intact. It shall be made sure that staff of TRF will behave in a polite and professional manner with fodder beneficiaries. Drinking water as well as seating arrangement shall be provided to the fodder beneficiaries.
- Fodder shall be handed over to only the listed beneficiary as per the record through which the token has been issued. Every beneficiary shall provide the issued fodder token with his/her CNIC. The verification officer will make sure that the fodder has been only issued to the actual beneficiary of the project.
- All the received counter-foils of the Fodder Token shall be collected by the staff of TRF and the same shall be submitted to the concerned Deputy Director L&F with copy of the information shall be provided to the District Distribution Committee.



### Project Completion Progress – Phase 2

Following is the list of the 88-field intervention staff currently hired for the project across 23 districts of the province:

| S # | Team Lead              | Designation          | CNIC Number   | Phone Number               | District  |
|-----|------------------------|----------------------|---------------|----------------------------|-----------|
| 1   | Mr. Ghulam Fareed      | Team Lead            | 4130666112413 | 03000360336                | Hyderabad |
| 2   | Mr. Paiyal             | logistic Coordinator | 4520842836741 | 3079214961                 |           |
|     |                        |                      |               | 3073009988                 |           |
| 3   | Mr. Rameez A Soomro    | Field Assistant      | 4120177544393 | 3213653579                 |           |
| 4   | Mr. Imtiaz Gul Chandio | Field Assistant      | 4130623115879 | 3153823164                 | Ghotki    |
| 5   | Dr. Riaz Ruk           | Team Lead            | 4510259800975 | 03133414833                |           |
| 6   | Mr. Mansub khoso       | logistic Coordinator | 4510494423009 | 03045839727                |           |
| 7   | Mr. Anwar Memon        | Field Assistant      | 4510246431355 | 3110003678                 |           |
| 8   | Mr. Saif Ur Rehman     | Field Assistant      | 4510284942469 | 3023155403                 | Kashmore  |
| 9   | Mr. Gul Muhammad       | Team Lead            | 4530303437149 | 03003966600                |           |
| 10  | Mr. Sarfraz Channa     | logistic Coordinator | 4310349391893 | 3113525427                 |           |
| 11  | Mr. Zakir Hussain      | Field Assistant      | 4310314228523 | 3013404278                 |           |
| 12  | Mr. Abdul Ghaffar      | Field Assistant      | 310324134735  | 3342614522                 | Jacobabad |
| 13  | Mr. Suresh Kumar       | Team Lead            | 4320328038851 | 03152202262<br>03463102380 |           |
| 14  | Mr. Saran Kumar        | logistic Coordinator | 4510222030557 | 0315-3769862               |           |
| 15  | Mr. Eshwar Chand       | Field Assistant      | 4320302492245 | 0310-8488895               |           |
| 16  | Mr. Ram Chand          | Field Assistant      | 4510214178853 | 0304-8304782               | Shikarpur |
| 17  | Mr. Asif Bhutto        | Team Lead            | 3320294033717 | 03008312430                |           |
| 18  | Mr. Abdul Raqeeb       | logistic Coordinator | 4330439122977 | 03003147971                |           |



|    |                          |                      |                 |             |                   |
|----|--------------------------|----------------------|-----------------|-------------|-------------------|
| 19 | Mr. Toufique Ahmed       | Field Assistant      | 4330439122977   | 03352283567 | Sukkur            |
| 20 | Mr. Ibrar Ali            | Field Assistant      | 4330453695887   | 03343928500 |                   |
| 21 | Dr Ghaffar Abbasi        | Team Lead            | 4550145906881   | 03072334298 |                   |
| 22 | Mr. Faizan Ahmed         | logistic Coordinator | 45501-7900295-9 | 3087449488  |                   |
| 23 | Mr. Tasneem Ahmed        | Field Assistant      | 45501-9306432-3 | 3048561727  |                   |
| 24 | Mr. Ali Hyder            | Field Assistant      | 45501-3958903-5 | 3070394805  | Larkana           |
| 25 | Dr. Zahid Hussain Shah   | Team Lead            | 4320321819575   | 03003429194 |                   |
| 26 | Mr. Fida Hussain Malgani | logistic Coordinator | 4320342375033   | 03073466796 |                   |
| 27 | Mr. Hasnain Mustafa      | Field Assistant      | 4320302764969   | 03170319556 |                   |
| 28 | Mr. Saqlain Hyder        | Field Assistant      | 432036652047    | 03173664109 |                   |
| 29 | Dr. Fazal M Kamalani     | Team Lead            | 4320222403625   | 03147123835 | Kamber Shahdadkot |
| 30 | Mr. Mohammad Ali         | logistic Coordinator | 4320255591677   | 03123309066 |                   |
| 31 | Mr. Abdul Jabar          | Field Assistant      | 4340204609833   | 3337519032  |                   |
| 32 | Mr. Mohammad Afzal       | Field Assistant      | 4340204910361   | 3151390303  |                   |
| 33 | Dr. Muhammad Usman       | Team Lead            | 4120322327595   | 03006562103 |                   |
| 34 | Mr. Mohd Hasan Babar     | logistic Coordinator | 41201-4426448-3 | 3003253659  | Dadu              |
| 35 | Mr. Manzoor H Mastoi     | Field Assistant      | 41202-4660184-5 | 3313285263  |                   |
| 36 | Mr. Azhar Farooque       | Field Assistant      | 41203-8297931-3 | 3053514074  |                   |
| 37 | Mr. Naresh Kumar         | Team Lead            | 41306-6911738-9 | 03433434878 |                   |
| 38 | Mr. Waqar Ali Shah       | logistic Coordinator | 41306-6163562-7 | 3232720661  |                   |
| 39 | Mr. Riaz Ali             | Field Assistant      | 41306-5341361-9 | 3433545691  | Jamshoro          |
| 40 | Mr. Sarfaraz Ali         | Field Assistant      | 44204-8718103-1 | 3183076663  |                   |



|    |                         |                      |                      |                                  |                        |
|----|-------------------------|----------------------|----------------------|----------------------------------|------------------------|
| 41 | Mr. Azam Kalhoro        | Team Lead            | .45301.087973<br>2.7 | 030049955<br>75                  | Naushehro Feroze       |
| 42 | Mr. M Afzal Kalhoro     | logistic Coordinator | 45301.7553571<br>.7  | 315371424<br>6                   |                        |
| 43 | Imtiaz Hussain          | Field Assistant      | 45301.0826679<br>.9. | 300377379<br>6<br>333278822<br>7 |                        |
| 44 | Naseer Ahmed            | Field Assistant      | 45301.9868326<br>.1. | 301226968<br>4                   |                        |
| 45 | Noor Mangi              | Team Lead            | 44204-<br>9980237-3  | 034536371<br>89                  | Sanghar                |
| 46 | Mr. Noor Hussain        | logistic Coordinator | 44203-<br>7229686-1  | 334288090<br>3                   |                        |
| 47 | Mr. Amanat Ali          | Field Assistant      | 44203-<br>8649894-5  | 308389646<br>9                   |                        |
| 48 | Mr. Shab Nawaz          | Field Assistant      | 44204-<br>5829767-9  | 305399211<br>9                   |                        |
| 49 | Dr. Jay Kumar           | Team Lead            | 413037729923<br>3    | 033329514<br>39                  | Mirpurkhas             |
| 50 | Mr. Mansoor Ali         | logistic Coordinator | 441045454377<br>77   | 346764784<br>8                   |                        |
| 51 | Mr. Muzammil Memon      | Field Assistant      | 413032735067<br>1    | 304546395<br>1                   |                        |
| 52 | Mr. Dhanesh Kumar       | Field Assistant      | 413032248823<br>1    | 304315522<br>1                   |                        |
| 53 | Dr. Vikesh Kumar        | Team Lead            | 41306-<br>5800974-3  | 033226349<br>33                  | Badin                  |
| 54 | Mr. Mohammad Awais      | logistic Coordinator | 41205-<br>7273926-3  | 0305-<br>5690298                 |                        |
| 55 | Mr. Sarfraz Ahmed Memon | Field Assistant      | 41101-<br>3413312-7  | 0347-<br>2366785                 |                        |
| 56 | Mr. Manshad Gadahi      | Field Assistant      | 41101-<br>5569101-0  | 0343-<br>1035856                 |                        |
| 57 | Dr. Ali Nawaz Jatt      | Team Lead            | 414019648655<br>5    | 030003570<br>08                  | Thatta 02 Deh of Malir |
| 58 | Mr. Mohd Ameen Arain    | logistic Coordinator | 41401-<br>2533297-9  | 341272935<br>8                   |                        |
| 59 | Mr. Fazal den           | Field Assistant      | 41401-<br>5667665-7  | 309240091<br>0                   |                        |
| 60 | Mr. Talib Jatt          | Field Assistant      | 41401-<br>7460080-9  | 341314672<br>1                   |                        |
| 61 | Dr. Hassan Raza Khawaja | Team Lead            | 414051401411<br>9    | 030002839<br>06                  | Sujawal                |



|    |                           |                      |                 |                          |                     |
|----|---------------------------|----------------------|-----------------|--------------------------|---------------------|
| 62 | Mr. Imtiaz Ahmed          | logistic Coordinator | 41405-8454358-1 | 3123324944               |                     |
| 63 | Mr. Imtiaz Ali Lashari    | Field Assistant      | 41408-2314081-5 | 3131316116<br>3085369597 |                     |
| 64 | Mr. Saleem Khaskheli      | Field Assistant      | 41408-3030007-7 | 3113152546<br>3023283023 |                     |
| 65 | Dr. Ismail Mari           | Team Lead            | 44202-4399093-1 | 03012619506              |                     |
| 66 | Mr. Muhammad Musawer      | logistic Coordinator | 41303-2727197-9 | 3463778790               | Umerkot             |
| 67 | Mr. Abdul Hafeez          | Field Assistant      | 44202-0963592-1 | 3461212616               |                     |
| 68 | Mr. Muhammad Hanif        | Field Assistant      | 44107-9829756-3 | 3442671800               |                     |
| 69 | Dr. Abdul Hussain Memon   | Team Lead            | 41308-9013357-3 | 03342051028              |                     |
| 70 | Mr. Farman Ali            | logistic Coordinator | 41308-7358787-5 | 3342808800               | Tando MK            |
| 71 | Mr. Abdul Razzaque        | Field Assistant      | 41602-0613669-1 | 3332806675               |                     |
| 72 | Mr. Muhammad Ismail       | Field Assistant      | 41603-0613090-3 | 3102656302               |                     |
| 73 | Mrs. Sanam Rajput         | Team Lead            | 41307-1340915-4 | 03326590550              |                     |
| 74 | Mr. Obaidullah            | logistic Coordinator | 41703-0616629-7 | 923063149522             | Tando Allahyar      |
| 75 | Mr. Saddam Hussain        | Field Assistant      | 41702-0613988-1 | 3123185383               |                     |
| 76 | Mr. Waseem                | Field Assistant      | 4170106820059   | 3253536293               |                     |
| 77 | Dr. Noor M. Ratarr        | Team Lead            | 4130313464513   | 03063000661              |                     |
| 78 | Dr Naveed shar            | logistic Coordinator | 4420580280319   | 3003079609               | Shaheed Benazirabad |
| 79 | Mr. Fayyaz                | Field Assistant      | 4120376357435   | 3004944907               |                     |
| 80 | Dr Shaharbano             | Field Assistant      | 4130373530976   | 3077980661               |                     |
| 81 | Mr. Shabbir Ahmed Jalbani | Team Lead            | 45104-2264267-3 | 03163264894              |                     |
|    |                           |                      |                 |                          | Khairpur            |



|        |                              |                         |                      |                  |        |
|--------|------------------------------|-------------------------|----------------------|------------------|--------|
| 8<br>2 | Mr. Saifullah<br>Langah      | logistic<br>Coordinator | 42501-069251-<br>3   | 0302-<br>2264929 |        |
| 8<br>3 | Mr.<br>Samiullah             | Field Assistant         | 45203-<br>6074072-1  | 0300-<br>9804846 |        |
| 8<br>4 | Mr. Habib Ur<br>Rehman       | Field Assistant         | 45201-<br>1392807-7  | 0308-<br>3293883 |        |
| 8<br>5 | Dr. Abdullah<br>Babar        | Team Lead               | 418010591871         | 030730955<br>69  |        |
| 8<br>6 | Mr.<br>Asadullah<br>Babar    | logistic<br>Coordinator | 41801-<br>0673909-1  | 304194872<br>7   | Matari |
| 8<br>7 | Dr Umer<br>Farooq<br>Panhwar | Field Assistant         | 41025-<br>1770813-7  | 303353402<br>1   |        |
| 8<br>8 | Dr Yaseen<br>Burriro         | Field Assistant         | 43206-<br>99308976-1 | 307030130<br>3   |        |



## Distribution Proforma & Fodder Distribution Token



لاڳيو اسٽاڪ اينڊ فشريز کاتو سنڌ



THE RISING FOUNDATION  
EMPOWER PEOPLE TO IMPROVE THEIR LIVELIHOOD

### ورهاست جي رپورٽ

جيئن ته اڄ تاريخ \_\_\_\_\_ ڏينهن \_\_\_\_\_ تي  
جانورن جي پالنا واري کاتي (لاڳيو اسٽاڪ ۽ فشريز) کاتو سنڌ پاران جانورن جي چاري جي  
ورهاست ڳوٺ \_\_\_\_\_ تعلقي \_\_\_\_\_ ضلعي \_\_\_\_\_ ۾  
ڪئي وئي، جنهن ۾ ضلعي جي هيٺين آفيسرن شرڪت ڪئي.

- 1، ڊپٽي ڊائريڪٽر لاڳيو اسٽاڪ ۽ فشريز کاتو ضلعو \_\_\_\_\_
- 2، \_\_\_\_\_
- 3، \_\_\_\_\_
- 4، \_\_\_\_\_
- 5، \_\_\_\_\_

مال جي چاري جي ورهاست لاءِ آيل متاثر مالوند ماڻهن کي تمام بهتر نموني سان عزت ۽  
احترام سان ويهاري کين ڏنل توڪن ذريعي مال جو چارو ڏنو ويو.  
ورهاست دوران ٽوٽل \_\_\_\_\_ وڏن جانورن لاءِ \_\_\_\_\_ مڻ بوهه (پوسو) ۽ ننڍن  
جانورن لاءِ \_\_\_\_\_ مڻ روڊ گراس تقسيم ڪيو ويو.

\_\_\_\_\_ تيمر ليبر.

\_\_\_\_\_ ضلعو



|                                                                                                                                                 |                                                                      |                                                                                     |                                                                     |
|-------------------------------------------------------------------------------------------------------------------------------------------------|----------------------------------------------------------------------|-------------------------------------------------------------------------------------|---------------------------------------------------------------------|
|                                                                | <b>Department of livestock and fisheries</b><br><b>Govt of Sindh</b> |  | THE RISING FOUNDATION<br>EMPOWER PEOPLE TO IMPROVE THEIR LIVELIHOOD |
| <b>Fodder Distribution In Calamity Affected Areas of Sindh</b>                                                                                  |                                                                      | Token No: <b>3703</b>                                                               |                                                                     |
| Department of livestock and fisheries Govt of Sindh                                                                                             |                                                                      |                                                                                     |                                                                     |
| Name of Beneficiary: _____ S/O: _____                                                                                                           |                                                                      |                                                                                     |                                                                     |
| CNIC No: _____ Cell No: _____ Village: _____                                                                                                    |                                                                      |                                                                                     |                                                                     |
| UC: _____ Taluka: _____ # of Small Animal : _____ # of Large Animals: _____                                                                     |                                                                      |                                                                                     |                                                                     |
| Wheat Straw: _____ Fodder, Rhodes Gross Required _____                                                                                          |                                                                      |                                                                                     |                                                                     |
| Distribution Point: _____ Date: _____ Day: _____                                                                                                |                                                                      |                                                                                     |                                                                     |
| Acknowledgment, I hereby confirm that the above specified quantity of Fodder (Wheat Straw/ Rhodes Gross) and this has also been narrated to me. |                                                                      |                                                                                     |                                                                     |
| Signature/ Thumb Impression<br>of beneficiary _____                                                                                             |                                                                      | Verified by<br>Logistics Coordinator<br>The Rising Foundation                       |                                                                     |

## **Project Completion (Phase 2) From 1<sup>st</sup> December 2022 to 28<sup>th</sup> February 2023**

Following is the cumulative progress achieved in 90 days of the project in designated 23 districts of Sindh province:

### **Data Collection of Flood stricken Livestock Farmers:**

Field intervention staff immediately started preparation to begin the data collection of monsoon rain flood effected farmers across the 23 districts of Sindh province in direct liaison with the concerned department of Livestock and Fisheries officers in their respective districts.

Meetings with district management officials to gather the location of displaced farmers were collected to ascertain the routes of access to collect the data of potential number of farmers to whom fodder, could be provisioned.

Data of large and small animals was collected along with household representation and the size of the herd. A need assessment of fodder was carried-out to ascertain the quantities required of wheat straw, Rhodes grass and silage.

This data reflects the fodder requirement for displaced farmers across 23 districts of Sindh province. The finalized list of beneficiaries provided to DoLF reflects fodder quantities are to be distributed for uninterrupted fodder supply to both large and small animals so that animal decline in health could be checked as well as their capacity to provide milk and meat could be sustained, if not improved.

### **Fodder Beneficiary Lists – 23 Districts:**

At completion of beneficiary survey of flood effected poor farmers, data was mapped and assembled based on districts and a fodder beneficiary list was provided to DoLF, GoS district officers for vetting and finalization.

### **Fodder Beneficiary Fodder Tokens issued:**

Once finalized data lists were provided from Deputy Directors of the DoLF at respective districts, fodder distribution tokens were generated in respective districts to be distributed among the fodder beneficiary farmers and beneficiaries were informed of the venue, date and timing of the fodder distribution.

### Fodder Supply Chain & Inter-provincial Fodder Transportation Management:

Fodder procurement and supply for the project has been managed by 1) M/s. Asasa Enterprises, 2) M/s. Gilani Multi-Buss, 3) M/s. Businesswire, 4) M/s. Panjtana, 5) M/s. Max Enterprises, 6) M/s. Ali-Ali, 7) M/s. Basit Enterprise, 8) M/s. S.A. Enterprise, and 9) M/s. Sharun International. While fodder transportation has been managed from the agricultural lands to the DoLF DHQ warehouses in respective 23 districts by M/s. Gorakh Tours & Travels.

### Fodder Processing & Fodder Distribution in 23 Districts:

The Rising Foundation (TRF) has been managing pre-delivery as well as post-delivery processing of the delivered fodder with direct support of respective DHQ offices of DoLF. It is worthwhile to endorse, the concerted efforts that have been put-forward by the fodder supply as well as transportation vendors through which The Rising Foundation has been able to timely process and fodder distribution to farmer beneficiaries across 23 districts of Sindh province.

Fodder distribution started as per the SOPs involved across majority of the districts simultaneously under direct supervision of the district-based staff of the Deputy Directors of Department of Livestock and Fisheries, Government of Sindh.

The fodder distribution was completed in all 23 districts of Sindh province by 28<sup>th</sup> February 2023. A total of **28,510 Metric Tons** of fodder with 27,510 Metric Tons of Wheat Straw for large animals and 1,000 Metric Tons of Rhodes Grass for small animals has been distributed among the 87,136 flood-affected farmers of 23 districts of Sindh by The Rising Foundation.

| Total Fodder Distributed in 23 Districts of Sindh Province |               |
|------------------------------------------------------------|---------------|
| Fodder Type                                                | Metric Tons   |
| Wheat Straw                                                | 27,510        |
| Rhodes Grass                                               | 1,000         |
| <b>Total</b>                                               | <b>28,510</b> |



### Fodder Distribution Status across 23 Districts


At the end of Phase – 1, the Department of Livestock & Fisheries, Government of Sindh assessed the lessons learnt in implementation of the initial phase of the project and re-directed its vendors and implementors with better strategy for the implementation of the Phase – 2 of the project to mitigate the delays and bottlenecks that occurred in Phase - 1.

Following recommendations were shared by the donor;

- The total duration of the Phase – 2 of the project was set at 90 days.
- Earlier the signatures of relevant areas Assistant Commissioner's were a compulsory requirement on the final approved list of the beneficiaries; but for Phase – 2 of the project this requirement was waived-off as it proved rather impossible in Phase – 1 of the Project to get sign-offs from the area concerned ACs both by the DoLF District staff as well as by the TRF field implementation teams.


With formal approval of the DoLF, TRF stepped in to implement the Phase – 2 of the project from 1<sup>st</sup> December 2022.

Following is the closeout status of fodder distribution in Phase – 2 of the project across 23 districts of Sindh, as of 28<sup>th</sup> February 2023; whereby a total of 27,509,982 kilo-grams of wheat straw and 1,000,006 kilo-grams of Rhodes grass was distributed.

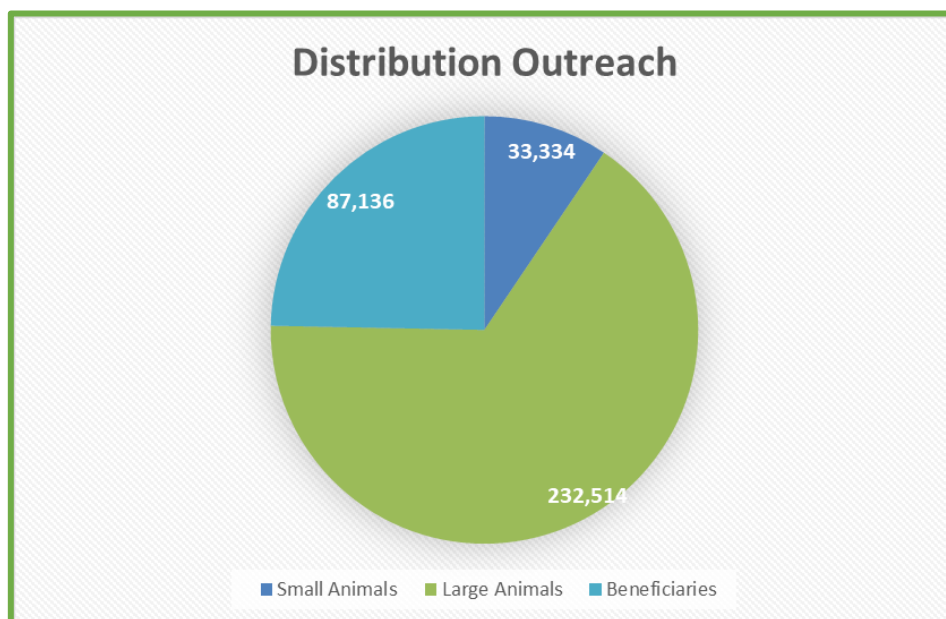




## District-wise Fodder Distribution (in Metric Tons) Phase 2

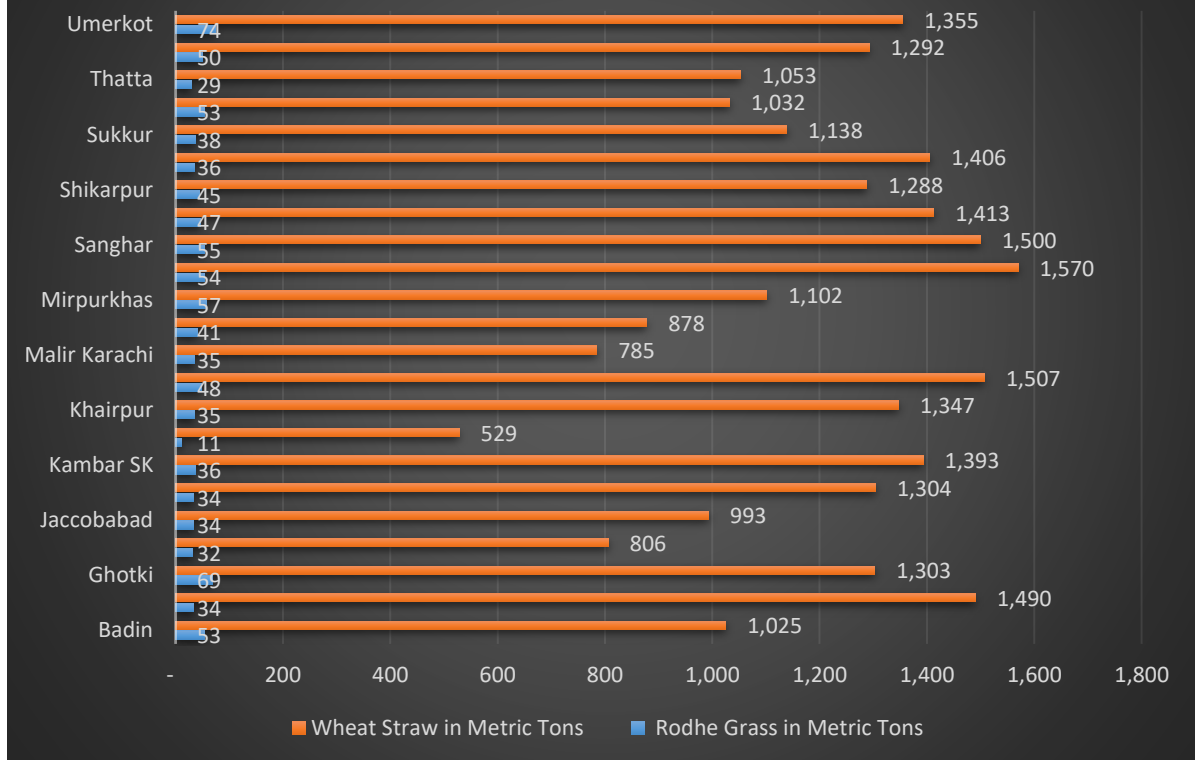


Thus, a total of 33,334 small animals and a total of 232,514 large animals have been provided with fodder provisioning for 15 days to offset the availability of fodder in 23 flood effected districts for the 87,136 poor small-holding livestock farmers.

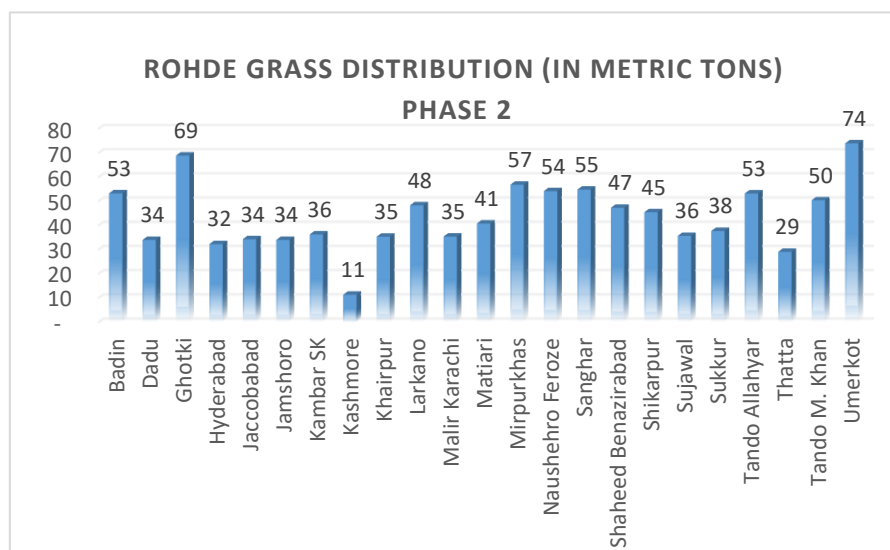



| S. No.             | District            | Fodder in KGs/M.Tons Delivered |                            |                    |                            |
|--------------------|---------------------|--------------------------------|----------------------------|--------------------|----------------------------|
|                    |                     | Rodhe Grass In KGs             | Rodhe Grass in Metric Tons | Wheat Straw in KGs | Wheat Straw in Metric Tons |
| 1                  | Badin               | 53,135                         | 53                         | 1,025,168          | 1,025                      |
| 2                  | Dadu                | 33,875                         | 34                         | 1,490,400          | 1,490                      |
| 3                  | Ghotki              | 68,740                         | 69                         | 1,303,118          | 1,303                      |
| 4                  | Hyderabad           | 32,145                         | 32                         | 806,398            | 806                        |
| 5                  | Jaccobabad          | 34,175                         | 34                         | 993,340            | 993                        |
| 6                  | Jamshoro            | 33,895                         | 34                         | 1,303,992          | 1,304                      |
| 7                  | Kambar SK           | 36,170                         | 36                         | 1,393,045          | 1,393                      |
| 8                  | Kashmore            | 11,250                         | 11                         | 528,895            | 529                        |
| 9                  | Khairpur            | 35,195                         | 35                         | 1,347,281          | 1,347                      |
| 10                 | Larkano             | 48,210                         | 48                         | 1,506,944          | 1,507                      |
| 11                 | Malir Karachi       | 35,285                         | 35                         | 785,085            | 785                        |
| 12                 | Matari              | 40,685                         | 41                         | 878,163            | 878                        |
| 13                 | Mirpurkhas          | 56,710                         | 57                         | 1,101,707          | 1,102                      |
| 14                 | Naushehro Feroze    | 54,065                         | 54                         | 1,569,741          | 1,570                      |
| 15                 | Sanghar             | 54,680                         | 55                         | 1,499,592          | 1,500                      |
| 16                 | Shaheed Benazirabad | 47,135                         | 47                         | 1,412,965          | 1,413                      |
| 17                 | Shikarpur           | 45,350                         | 45                         | 1,288,158          | 1,288                      |
| 18                 | Sujawal             | 35,540                         | 36                         | 1,405,662          | 1,406                      |
| 19                 | Sukkur              | 37,585                         | 38                         | 1,138,365          | 1,138                      |
| 20                 | Tando Allahyar      | 53,095                         | 53                         | 1,032,008          | 1,032                      |
| 21                 | Thatta              | 28,966                         | 29                         | 1,052,822          | 1,053                      |
| 22                 | Tando M. Khan       | 50,325                         | 50                         | 1,292,184          | 1,292                      |
| 23                 | Umerkot             | 73,795                         | 74                         | 1,354,950          | 1,355                      |
| <b>Grand Total</b> |                     | <b>1,000,006</b>               | <b>1,000</b>               | <b>27,509,982</b>  | <b>27,510</b>              |

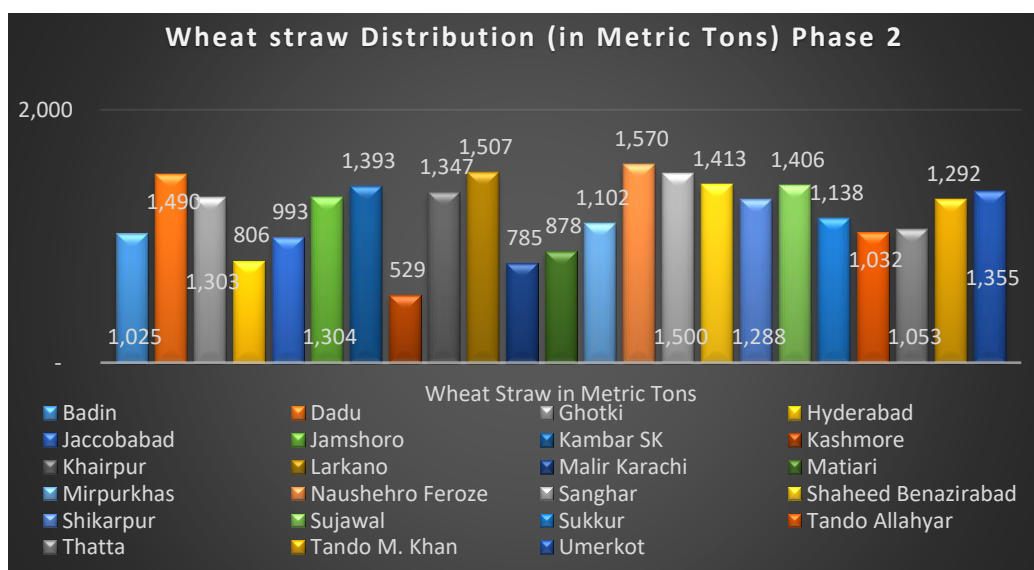



### Beneficiaries Outreach vis-a-vie Livestock Catered

| S. No.             | District            | Animals Catered/Beneficiaries Reached |                       |                      |
|--------------------|---------------------|---------------------------------------|-----------------------|----------------------|
|                    |                     | Small Animals Catered                 | Large Animals Catered | Nos of Beneficiaries |
| 1                  | Badin               | 1,771                                 | 13,669                | 1,956                |
| 2                  | Dadu                | 1,129                                 | 19,872                | 2,745                |
| 3                  | Ghotki              | 2,291                                 | 17,375                | 4,017                |
| 4                  | Hyderabad           | 1,072                                 | 10,752                | 3,957                |
| 5                  | Jacobabad           | 1,139                                 | 13,245                | 3,026                |
| 6                  | Jamshoro            | 1,130                                 | 17,387                | 3,525                |
| 7                  | Kambar SK           | 1,206                                 | 18,574                | 4,167                |
| 8                  | Kashmore            | 375                                   | 7,052                 | 1,591                |
| 9                  | Khairpur            | 1,173                                 | 17,964                | 4,164                |
| 10                 | Larkano             | 1,607                                 | 20,093                | 3,442                |
| 11                 | Malir Karachi       | 1,176                                 | 10,468                | 2,598                |
| 12                 | Matiari             | 1,356                                 | 11,709                | 4,488                |
| 13                 | Mirpurkhas          | 1,890                                 | 14,689                | 3,889                |
| 14                 | Naushehro Feroze    | 1,802                                 | 20,930                | 5,103                |
| 15                 | Sanghar             | 1,823                                 | 19,995                | 11,922               |
| 16                 | Shaheed Benazirabad | 1,571                                 | 18,840                | 6,390                |
| 17                 | Shikarpur           | 1,512                                 | 17,175                | 2,961                |
| 18                 | Sujawal             | 1,185                                 | 18,742                | 3,050                |
| 19                 | Sukkur              | 1,253                                 | 15,178                | 3,318                |
| 20                 | Tando Allahyar      | 1,770                                 | 13,760                | 1,046                |
| 21                 | Thatta              | 966                                   | 14,038                | 2,926                |
| 22                 | Tando M. Khan       | 1,678                                 | 17,229                | 2,696                |
| 23                 | Umerkot             | 2,460                                 | 18,066                | 4,159                |
| <b>Grand Total</b> |                     | <b>33,334</b>                         | <b>232,514</b>        | <b>87,136</b>        |



## Project's Photo Gallery



**Project Completion Report (Phase-2):** Service Consultancy for Provision of Fodder for Livestock of Monsoon Rain Flood Calamity Hit Areas of Sindh Province – Project (Livestock Department Sindh).









**Project Completion Report (Phase-2):** Service Consultancy for Provision of Fodder for Livestock of Monsoon Rain Flood Calamity Hit Areas of Sindh Province – Project (Livestock Department Sindh).
